


## Monthly Report April 2020

### Facilities Assessment and Long Range Plan

Information Item was presented at the March Board Meeting.

Citizens' Bond Committee will utilize the data to create the 2020 Bond.

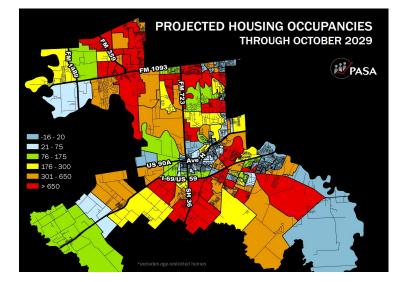

### Dr. Thomas E. Randle High School & Harry Wright Junior High School

Site development, field turf, steel erection, roofing, and framing are in progress.

Schools are on schedule to open in August 2021.



### Traylor Stadium Press Box Replacement

Construction is underway.

Scheduled for completion in August 2020.



### Transportation Fuel Tank Replacement

Morris & Associates is the A/E Firm of Record.

Contractor recommendation is on the April Board Agenda.



### Jane Long Historic Gym Renovations

VLK is the Architect of Record.

Advertisements have been published.

Contractor recommendation will be on the May Board Agenda.



### ALC/1621 Additions and Renovations

VLK is the Architect of Record.

Advertisements have been published.

Contractor recommendation will be on the May Board Agenda.



### Lamar CHS & Lamar JHS Additions & Renovations

PBK is the Architect of Record.

Design Development is on the April Board Agenda.



# Terry HS & George JHS Additions & Renovations

VLK Architects is the Architect of Record.

Construction documents are being developed.



### Multi-Campus Carpet Replacement

Corgan is the Architect of Record.

Construction Phase is underway.

Contractor is ordering materials to begin installation in June.



### Multi-Campus Improvements & HVAC Controls Upgrades

Corgan is the Architect of Record.

Construction Phase is underway.

Contractor is ordering materials to begin installation in June.

### Multi-Purpose Space (HS) & Orchestra (MS) Additions

PBK is the Architect of Record.

Contractor recommendation will be on the May Board Agenda.





### **Brazos Crossing Exterior Improvement**

VLK is the Architect of Record.

Design Development will be presented at the May Board Meeting.



### to boo December 2010 to the top off Cancer to the top off Cancer top off Cancer FLETCHER FLETCHER The top off Cancer FLETCHER The top off Cancer FLETCHER The top off Cancer Th

### Fletcher Morgan, Jr. Elementary School

Advertisements have been published.

Contractor recommendation will be on the May Board Agenda.

Property is located on FM 1093 across from the Weston Lakes subdivision main entry.

School is scheduled to open in August 2021.

2017 BOND REFERENDUM SUMMARY									
PROJECT NAME	ORIGINAL BUDGET	BUDGET CHANGE	PROJECT BUDGET	COMMITTED	BALANCE				
Austin ES Re-Roof	\$1,900,000.00	\$0.00	\$1,900,000.00	\$897,273.00	\$1,002,727.00				
Seguin ECC Re-Roof	\$1,900,000.00	\$0.00	\$1,900,000.00	\$982,961.00	\$917,039.00				
Terry HS Serving Lines	\$680,000.00	\$0.00	\$680,000.00	\$656,123.95	\$23,876.05				
George JHS Serving Lines	\$620,000.00	\$0.00	\$620,000.00	\$528,728.39	\$91,271.61				
Classroom Intruder Locks	\$400,000.00	\$0.00	\$400,000.00	\$390,985.72	\$9,014.28				
High School LOTE Lab Renovations	\$1,050,000.00	\$0.00	\$1,050,000.00	\$198,565.00	\$851,435.00				
ES Cooler/Freezer Replacement	\$1,400,000.00	\$0.00	\$1,400,000.00	\$1,230,756.00	\$169,244.00				
Camp. ES, Will. ES, Nav. MS & Wess. MS Improv.	\$2,740,000.00	\$114,000.00	\$2,854,000.00	\$2,824,511.64	\$29,488.36				
HS Field Turf Replace & Foster HS Track	\$9,082,719.00	\$0.00	\$9,082,719.00	\$7,346,973.72	\$1,735,745.28				
Foster HS Athletic Improvements	\$867,281.00	\$0.00	\$867,281.00	\$829,768.00	\$37,513.00				
Dr. Thomas E. Randle High School	\$126,500,000.00	\$0.00	\$126,500,000.00	\$111,845,509.73	\$14,654,490.27				
Harry Wright Junior High School	\$62,000,000.00	\$0.00	\$62,000,000.00	\$53,089,617.82	\$8,910,382.18				
Lamar CHS & Lamar JHS Exterior Improvements	\$10,840,000.00	\$0.00	\$10,840,000.00	\$611,015.00	\$10,228,985.00				
Lamar CHS & Lamar JHS Additions & Renovations	\$12,980,000.00	\$0.00	\$12,980,000.00	\$653,031.00	\$12,326,969.00				
Terry HS & George JHS Additions & Renovations	\$14,650,000.00	\$0.00	\$14,650,000.00	\$752,390.00	\$13,897,610.00				
Traylor Stadium Press Box Replacement	\$2,800,000.00	\$1,632,000.00	\$4,432,000.00	\$4,340,773.00	\$91,227.00				
New Alternative Learning Center	\$12,200,000.00	\$0.00	\$12,200,000.00	\$661,110.00	\$11,538,890.00				
Jane Long ES Historical Gym Renovations	\$3,200,000.00	\$0.00	\$3,200,000.00	\$363,604.00	\$2,836,396.00				
Jane Long Auditorium Seating	\$125,000.00	\$0.00	\$125,000.00	\$0.00	\$125,000.00				
Transportation - Replace Underground Fuel Tank	\$900,000.00	\$0.00	\$900,000.00	\$145,164.00	\$754,836.00				
HS Multi-Purpose Rooms & MS Orchestra Adds	\$9,450,000.00	\$0.00	\$9,450,000.00	\$338,120.00	\$9,111,880.00				
Multi-Campus Carpet Replacement	\$2,310,000.00	\$0.00	\$2,310,000.00	\$104,800.00	\$2,205,200.00				
Multi-Campus ES Renovations	\$3,370,000.00	\$0.00	\$3,370,000.00	\$114,450.00	\$3,255,550.00				
Brazos Crossing Renovations	\$1,800,000.00	\$0.00	\$1,800,000.00	\$114,750.00	\$1,685,250.00				
Morgan Elementary School	\$30,200,000.00	\$0.00	\$30,200,000.00	\$0.00	\$30,200,000.00				
New Elementary School #30	\$32,600,000.00	\$0.00	\$32,600,000.00	\$0.00	\$32,600,000.00				
New Elementary School #31	\$35,200,000.00	\$0.00	\$35,200,000.00	\$0.00	\$35,200,000.00				

2017 BOND TECHNOLOGY SUMMARY									
PROJECT NAME	ORIGINAL BUDGET	BUDGET CHANGE	PROJECT BUDGET	COMMITTED	BALANCE				
IFP-Interactive Flat Panel	\$9,044,000.00	\$0.00		\$5,037,430.83	\$4,006,569.17				
PTO-Printer Refresh	\$1,440,000.00	\$0.00		\$1,348,510.04	\$91,489.96				
CCU-Campus Core Uplink	\$740,000.00	\$0.00		\$638,018.83	\$101,981.17				
ESO-Expanded Storage	\$400,000.00	\$0.00		\$400,000.00	\$0.00				
SCO-Security Cameras	\$250,000.00	\$0.00		\$250,000.00	\$0.00				
TEL-Telephones	\$890,000.00	\$0.00		\$697,671.96	\$192,328.04				
CR0-Computer Refresh	\$18,344,000.00	\$0.00		\$7,785,565.69	\$10,558,434.31				
LCO-Laptop Carts	\$450,000.00	\$0.00		\$0.00	\$450,000.00				
SCN-Eduphoria Scanners	\$122,000.00	\$0.00		\$121,450.00	\$550.00				
IA0-Interact	\$2,646,000.00	\$0.00		\$0.00	\$2,646,000.00				
TOTAL	\$34,326,000.00			\$16,278,647.35	\$18,047,352.65				
TOTAL TECHNOLOGY BOND	\$34,326,000.00								
REMAINING TECHNOLOGY BOND	\$18,047,352.65								

2017 BOND TRANSPORTATION SUMMARY										
PROJECT NAME	ORIGINAL BUDGET	BUDGET CHANGE	PROJECT BUDGET	COMMITTED	BALANCE					
New Bus Purchase	\$2,560,746.00	\$0.00	\$2,560,746.00	\$2,560,746.00	\$0.00					
Smart Tag	\$500,000.00	\$7,300.00	\$507,300.00	\$507,250.91	\$49.09					

### LAMAR CISD 2017 BOND PROGRAM - PROJECT LIST

	2018	2019			2020		2	021		2022		2023	
PROJECTS	SEPT OCT DEC JAN JAN APR APR MAY		SEPT OCT NOV DEC	JAN FEB MAR APR		SEPT SEPT OCT NOV DEC			SEPT OCT DEC DEC JAN AAR APR		DEC JAN		SEPT OCT NOV DEC
Austin ES & Seguin ES Re-Roof													
Terry HS & George JHS Serving Lines	CONSTRUCTION		WARRANT	Y									
Classroom Intruder Locksets	CONSTRUCTION WAR	RANTY.											
High School Artificial Turf & Tracks	D CD P CONS	7	WARRANT	Y									
Foster HS Athletic Improvements	D CD P CONS	1	WARRANT	Y									
CES, WES, WMS, NMS Improv.		3	WARRANT	Y									
ES Cooler/Freezer Replacement	D CD P CC	wst	WARRANT	Y									
High School LOTE Lab Installation	D P C	nast W	ARRANTY										
Fuel Tank Replacement		p	CD P	CONST		WARRANTY	(						
Traylor Stadium Pressbox	DESIGN	c	D P CC	ONSTRUCTION	4	WARRANTY	(						
Austin, Bowie, D. Smith, T. Ray & Jackson Improv.*			d CD	P CONST		WARRANTY	e						
FHS, BJHS, JES, PES, LES Improv.*			d <mark>CD</mark>	P CONST		WARRANTY	6						
Jane Long Auditorium Seating				CD P	CB467	WARRANTY	e						
Jane Long Historical Gym Renovations	ات ا	SIGN	CD	P CONSTRU	CTICHI	WARF	RANTY						
ALC Additions & Renovations	Di	esign	CI	D P C	X34957			X	ARRANTY				
Elementary (#29)*		D	CD	P CONSTRU	стон			VARRA	NTY				
Elementary (#30)*					Þ	CD	P CONSTRUCT	ØN		WARRANT	γ		
Elementary (#31)*					Þ	CD	P CONSTRUCT	IQIN(		WARRANT	γ		
Randle High School & Wright Junior High	D <mark>CD </mark> P	CONSTR	UCTION					WAR	RANTY				
Lamar Complex Exterior Improvements	DESIGN			CD	P cor			Х	ARRANTY				
Lamar HS & JHS Add & Renov.*			DESIGN	CD	P cor	STRUCTION		W	ARRANTY				
Terry HS & GJHS Add & Renov.*			DESIGN	CD	P COI	INTRUCTION		W	ARRANTY				
HS Multi-Purpose* MS Orchestra Additions			DES	IGN CD		P CONSTR	UCTION	X	ARRANTY				
Brazos Crossing Exterior*			DES	IGN CD		P CONSTR	UCTION	W	ARRANTY				
	SEPT OCT NDV DEC JAN FEB MAR APR		SEPT DCT NOV DEC	JAN FEB MAR APR		SEPT SEPT OCT NOV DEC			SEPT OCT NOV DEC JAN FEB MAR APR		DEC DEC		SEPT DCT NOV DEC
	2018	2019			2020		2	021		2022		2023	
